
REPORTNOW
CHANGE MANAGEMENT PLAN

Version 1.0

29/10/2025

Prepared by Team TEL5 Team 2

Dylan Quek Zhi En

Ang Wei Ming

Chi Seo Hyeon

Choo Kean Yee

Madelyn Cruz Tan

Lim Jun Howe

Tan Yong Huat

VERSION HISTORY

Version #	Implemented By	Revision Date	Approved By	Approval Date	Reason
1.0	Tan Yong Huat	29/10/2025	Madelyn Cruz Tan	29/10/2025	Initial Change Management Plan

TABLE OF CONTENTS

1 INTRODUCTION	4
1.1 Purpose of The Change Management Plan	5
2 CHANGE MANAGEMENT PROCESS	5
2.1 Change Request Process Flow Requirements	5
2.2 Change Request Form and Change Management Log	6
2.3 Evaluating and Authorizing Change Requests	7
3 Responsibilities	8
APPENDIX A: CHANGE MANAGEMENT PLAN APPROVAL	9
APPENDIX B: REFERENCES	10
APPENDIX C: KEY TERMS	11
APPENDIX D: CHANGE REQUEST FORM EXAMPLE	12
APPENDIX E: CHANGE MANAGEMENT LOG TEMPLATE	13

1 INTRODUCTION

1.1 PURPOSE OF THE CHANGE MANAGEMENT PLAN

The Change Management Plan outlines the approach for managing and controlling project changes throughout the lifecycle of the ReportNow platform from planning to deployment. It ensures that all proposed modifications to scope, schedule, resources, and deliverables are properly evaluated, approved, and documented.

This plan supports consistent decision-making, minimizes disruption to development, and promotes transparency among stakeholders. It serves as a guide for the project manager, development team and the quality assurance team in ensuring that changes contribute positively to ReportNow's mission of delivering a reliable, user-friendly, and intelligent public issue reporting system for Singapore.


2 CHANGE MANAGEMENT PROCESS

The Change Management process establishes an orderly and effective procedure for tracking the submission, coordination, review, evaluation, categorization, and approval of all changes to the ReportNow project baselines to ensure stability and alignment with project objectives.

2.1 CHANGE REQUEST PROCESS FLOW REQUIREMENTS

Step	Description
Generate	A submitter completes a Change Request (CR) Form and sends it to the QA Manager, who acts as the Change Manager for the ReportNow project. The QA Manager will ensure that the request is complete and relevant before proceeding.
Cost	The Project Manager will assess any potential resource or time implications. Where applicable, the Project Manager may consult the Release Manager to determine the feasibility of implementing the change within existing constraints.
Evaluate and Authorize	The Change Review Team, comprising the Project Manager, QA Manager, and Lead Developer, will review each CR to evaluate its impact on scope, schedule, and quality. For critical or high-priority changes, the team will decide collectively whether to authorize implementation.
Log	Once reviewed, the CR will be recorded in the Change Management Log by the QA Manager. The log will be updated throughout the process to reflect each request's status, actions taken, and resolution.
Implement	Upon approval, the development team (Front-end, Back-end, and Lead Developer) will make the necessary code or configuration adjustments. Progress and completion will be communicated to the QA Manager and Project Manager.
Integrate and Validate	After implementation, the QA Engineer will test and validate that the changes meet functional and quality requirements. The QA Manager will ensure all validations are documented before integration into the production environment.
Close	The QA Manager will close the CR once validation is complete and all documentation has been reviewed. The closure confirms that the requested change was properly implemented, tested, and approved by relevant stakeholders.

The flowchart shown in the next page depicts the procedure to request and implement changes to our project and application.

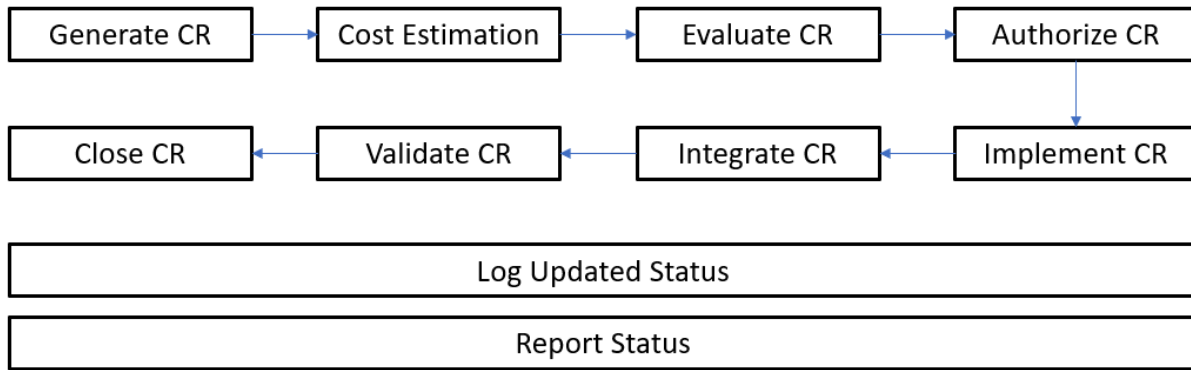

2.2 CHANGE REQUEST FORM AND CHANGE MANAGEMENT LOG

Element	Description
CR#	Assigned by the Change Manager. Format of CR will be XX-0001 where XX represents the document to be changed followed by the change number (e.g., RM-005 for the 5 th change request made for the Risk Management Plan)
Request Title	A brief description of the CR
Requestor Name	Name of the person completing the CR Form and who can answer questions regarding the suggested change
Current Version	The product version that the suggested change is for
New Version	The proposed product version after the change
Contact Information	Contact information about the submitter
Description of Request	Description of the desired change, the impact, or benefits of a change should also be described
Date Submitted	The date the CR was submitted to the Change Control Board
Date Required	The date the CR must be completed by
Change Priority	A code that provides a recommended categorization of the urgency of the requested change (Critical, High, Medium, Low)
Product	The product that the suggested change is for
Reason(s) for Change	Reason(s) for the change to be made
Initial Impact Analysis	Initial analysis on how the requested change will affect impact areas
Components Impacted	List of components affected by the requested change
Estimated Time Required	The estimated time required for the change(s) to be made
Estimated Cost Required	The estimated cost required for the change(s) to be made
Change Implementation	Who will make the changes and what changes must be made to what components
Quality Assurance/Testing	The planned tests to be run on the proposed changes before it will be accepted into the system

2.3 EVALUATING AND AUTHORIZING CHANGE REQUESTS

Change requests are evaluated using the following priority criteria:

Priority	Description
Critical	Reserved for the most critical change(s) to the foundation or a core component of our project which will impact most of the stakeholders. Requires a decision from the Change Control Board within one working day from the date of CR submission.
High	Potentially damaging codes that have a wide impact on the other functionalities of the program. CR must be implemented within 10 days.
Medium	Repairment of missing functionalities or additional of functionalities requested by the clients. CR must be implemented within 2 weeks.
Low	Minor change(s) which will have little or insignificant impact on the product. Mainly cosmetic changes with no impact on other artifacts of the project. No stipulated deadline for approval of such requests.

Change requests are evaluated and assigned one or more of the following change types:

Type	Description
Scope	Change affecting scope
Time	Change affecting time
Duration	Change affecting duration
Cost	Change affecting cost
Resources	Change affecting resources
Deliverables	Change affecting deliverables
Product	Change affecting product
Processes	Change affecting process
Quality	Change affecting quality

Change requests are evaluated and assigned one of the following status types:

Status	Description
Open	Entered/Open but not yet approved or assigned
Work in Progress	CR approved, assigned, and work is progressing
Rejected	CR rejected and closed
Testing	CR work has been completed and is in the testing phase
In Review	Testing completed and is pending final review from Project Manager before release.
Closed	CR work is complete, has passed all tests, and updates have been released.

3 RESPONSIBILITIES

Role	Name	Contact	Description
Project Manager	Madelyn Cruz Tan	marv0006@e.ntu.edu.sg	Final approving authority for all Change Requests. Evaluates feasibility, resource use, and alignment with project objectives.
QA/Change Manager	Tan Yong Huat	ta0008at@e.ntu.edu.sg	Oversees the change process, verifies CR completeness, maintains the Change Log, and ensures proper validation and closure.
Lead Developer	Ang Wei Ming	wang048@e.ntu.edu.sg	Approves and advises on all technical changes. Ensures system integrity and adherence to development standards.
QA Engineer	Choo Kean Yee	kchoo011@e.ntu.edu.sg	Tests and validates implemented changes. Confirms that functionality and quality standards are met.
Front-end Developer	Dylan Quek Zhi En	dy0001en@e.ntu.edu.sg	Implements approved UI or client-side changes and reports progress to the QA Manager.
Back-end Developer	Chi Seo Hyeon	seohyeon001@e.ntu.edu.sg	Implements approved server-side or database changes and ensures system stability during updates.
Release Manager/Engineer	Lim Jun Howe	jlim480@e.ntu.edu.sg	Coordinates deployment of approved changes. Ensures release packages are versioned, stable, and properly integrated before going live.

APPENDIX A: CHANGE MANAGEMENT PLAN APPROVAL

The undersigned acknowledge they have reviewed the ReportNow **Change Management Plan** and agree with the approach it presents. Changes to this **Change Management Plan** will be coordinated with and approved by the undersigned or their designated representatives.

Signature:



Date: 29/10/2025

Print Name:

Madelyn Cruz Tan

Role:

Project Manager

Signature:



Date: 29/10/2025

Print Name:

Tan Yong Huat

Role:

QA Manager

Signature:



Date: 29/10/2025

Print Name:

Choo Kean Yee

Role:

QA Engineer

APPENDIX B: REFERENCES

The following table summarizes the documents referenced in this document.

Document Name and Version	Description	Location
CDC_UP_Change_Management_Plan_Template	Initial Template	-
LarkDetect_Change_Management_Plan_v1.0	LarkDetect Change Management Plan	-

APPENDIX C: KEY TERMS

The following table provides definitions for terms relevant to this document.

Term	Definition
Authorization	Official permission to access a specific system or to carry out a specific function/task/change.
Change Management	A committee that evaluates and prioritizes change requests in the context of projects. Change Management A project management plan that has authority to approve or reject the changes on the project.
Change Request (CR)	A formal proposal for modifications to the software system. Only formally documented requested changes are processed, and only approved change requests are implemented.
Change Request Form (CRF)	A form that is used to request a change in the project.
Project Manager	The person in overall charge of the planning and execution of a project.

APPENDIX D: CHANGE REQUEST FORM EXAMPLE

The example Change Request Form attached below can be used to submit changes during the life of the project.

*Change Request Form**Version: 1.0***Change Request Form**

GENERAL INFORMATION				
CR#	[To be filled by Change Manager]			
Request Title				
Requestor Name				
Current Version				
New Version				
Contact Information				
Description of Request				
Date Submitted				
Date Required				
Change Priority	☐ Low	☐ Medium	☐ High	☐ Critical
Reason(s) for Change				
Initial Impact Analysis				
Components Impacted				
Estimated Time Required				
Estimated Cost Required	☐ Recommended ☐ Not Recommended [To be filled by Project Manager]			
Change Implementation				
Quality Assurance/Testing				
Comments and Recommendations	▼			

PROJECT MANAGER - DECISION				
Decision	☐ Approved	☐ Approved w/Conditions	☐ Rejected	☐ More Info
Decision Date				
Decision Explanation				
Conditions				

